

P11 Dashboard


Weekly Summary

This week, the team completed several important account related features. The logout and account deletion functions were successfully implemented, and the system now supports editing account details through a newly added update feature. These additions strengthen the overall user account management workflow and move the project closer to a functional end-to-end user experience. However, despite this progress, it has become increasingly clear that the current project deadline is unlikely to be met. Several remaining components still require development, testing, and integration time, and the pace of recent progress suggests that the original timeline may have been too optimistic. The team may need to discuss timeline adjustments or prioritize remaining features to ensure a stable and polished final product.

Recent Deliverables Completed

ID	Name	Owner	Notes
3.1.2.1	Add functions for logout and delete account	Gabriel Traas	
3.1.2.2	Add function to edit account details	Ashton Raber	
3.1.3.1	Find 10 upcoming events to add to database	Ashton Raber, Gabriel Traas	
3.1.3.5	Add event creation and deletion for admins and event hosts	Gabriel Traas	Functionality: Only event hosts can create events and delete there own events. Admins can delete any event they want but cannot create events.

Deliverables Status

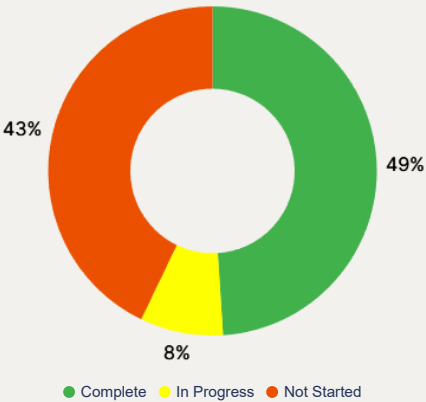

Gantt Chart Timeline

🔍 🔍 Months 📅



Risks Report

ID	Risk Name	Description	Impact	Probability	Mitigation/ Response Plan	Notes/ Updates
3	Underestimating testing time	The debugging and integration testing of the project takes longer than anticipated.	Medium	Medium	Allocate more time to testing and start testing in parallel with development.	
4	Performance bottlenecks	The search or RSVP actions may exceed the 2 second performance requirement.	Low	Medium	Optimize queries and caching and test the performance under simulated loads early on in the project.	
1	Extreme winter conditions preventing team coordination	Canadians winters way impede vesicles used to get to team and sponsor meeting.	Medium	Low	Have winter tires and be prepared for Canadian winters and the risks thereof. Failing that, a method to meet online can be prepared to use if in person meetings become impossible, presently that will be the project Discord.	

Deadline Report

ID	Description	Submitter	Revised Finish Date	Reason for Change	Impact Analysis	Approved By

Decisions Report

ID	Date of Decision	Description	Decision Made	Decision Maker(s)	Reason for Decision
2	11/26/25	Admin Event Creation	The ability for admins to create events has been removed.	Ashton Raber	Admins should only monitor the site and should not have the ability to add events. If they wish to create an event, they must create a host profile.

Issues Report

ID	Issue Name	Description	Status	Impact	Mitigation/ Response Plan	Date Identified
6	Deadlines can not be meet	The development of the OkanaganConnect website has taken longer than expected due to the development team busy schedule.	In Progress	High	The team will finish their assignments early so that they can get as much done for the project as possible.	12/01/25
1	Insufficient Developer Training	There are some programs and techstack items that no present developer within the project has used before, or which we are actively learning in other classes, this could potentially lead to slower production times as we learn the systems before they can be implemented.	In Progress	Medium	Each individual is responsible for their own training, with an understanding that we will reach out to each other in the event that the issue is begins to resulting in the slowing of production times. In this event additional manpower and expertise can be lent to that developer.	10/26/25

Deliverables Report

ID	Name	Status	% Complete	Owner	Planned Finish Date
3.1.2.3	Add functionality to frontend for user functions	In Progress	70	Ashton Raber, Dan Williams	11/06/25
3.1.3.2	Add functions to create, edit and attend events to backend	In Progress	80	Dan Williams	11/03/25
3.1.3.4	Add search event function to backend	In Progress	0	Dan Williams, Gabriel Traas	11/17/25
3.1.3.6	Add functionality to frontend for event functions	In Progress	80	Ashton Raber, Gabriel Traas	11/06/25

Scope Changes Report

ID	Description	Reason for Change	Submission Date	Impact Analysis

