

P5 - Team Sprint Meeting

~~Repo Link: https://github.ubc.ca/COSC_O_305_101_O2025W1/L03_Scrum_Coke~~

L03-Scrum&Coke

Dan Williams

Ashton Raber

Gabriel Traas

1.

- Deliverables:
 - Risk identified - In Progress
 - Wireframe - Complete
 - Dashboard Framework - Complete
- Next Weeks Deliverables
 - None mandatory - Time has been allotted for midterm studying, this was expected and planned for.
- Scope Changes:
 - There have been no changes in scope this week
- Deadline Changes:
 - There have been no changes to the deadlines so far.
- Decisions Made
 - Tech Stack selected

- Risk and Risk Mitigation



Risk	Mitigation
Lack of knowledge of software may slow down work rate	We will put in extra hours of studying to learn the different APIs (Training for developers)

- Issues, lasting effect and solutions

Issue	Effects	Solution
Team member illness	Some tasks this week did not have an able task owner, delays in task delivery	Redistribute the work load

Summary: Our smartsheet monitoring is not where it needs to be. Difficult to track progress. Sickness prevented us from getting all desired tasks completed. Plan for next week is to hold a meeting and adjust our timelines.

DELIVERABLES

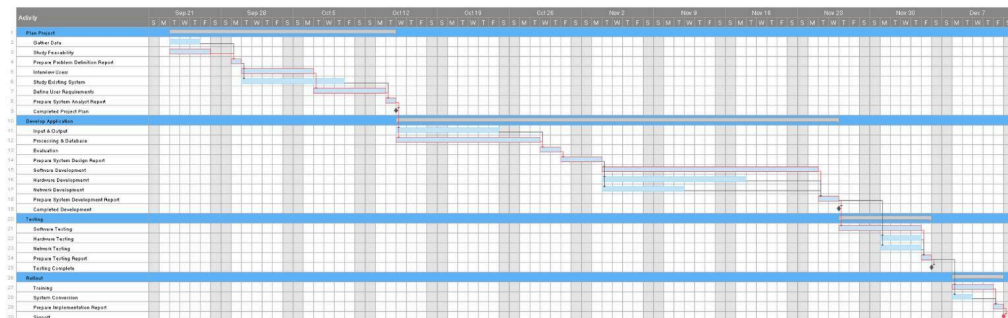

DAN

Complete: None

In Progress: Request Form, Reports, Dashboards

NOTES:

GABRIEL

Complete: None

In Progress: Risk Identification, Wireframe

NOTES:

WAS SICK THIS WEEK

ASHTON

Complete: None

In Progress: Request Form, Reports, Dashboards

NOTES:

ISSUES

Lack of team meetings
Member Sickness
Smartsheet Monitoring

MITIGATIONS

Schedule team meetings
Reallocate workload
Assign as priority for next week

RISKS

Falling Behind
Dealing with reduced workers
has caused us to fall behind.
Readjust timelines to fit

Unbalanced Workload
Redo schedule balance
