

P7 Dashboard


Weekly Summary

During the first week of the two-week sprint to develop the complete UI prototype, the team made significant progress and successfully completed all planned frontend development tasks. The goal was to design and implement the user interface components and ensure that the overall look and feel align with the project's design specifications and user experience goals. Next week we will be making the 3-5 minute video for the executive sponsor.

Recent Deliverables Completed

ID	Name	Owner	Notes
2.2.1	Main Colors Selected (Graphical Design Format Made)	Ashton Raber, Dan Williams	
2.2.2	Fonts and Themes Selected	Gabriel Traas	

Deliverables Status

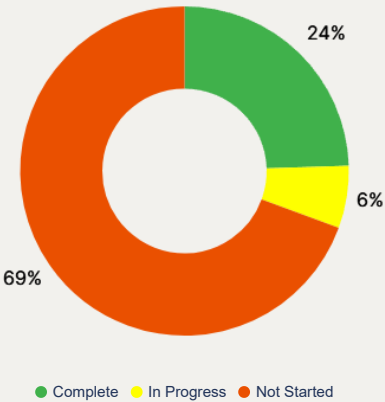

Gantt Chart Timeline

🔍 📅 Months 📅



Risks Report

ID	Risk Name	Description	Impact	Probability	Mitigation/ Response Plan	Notes/ Updates
2	Deadlines cannot be met	The deadlines of project deliverables are imminent and the development team agrees it is unlikely to be accomplished without extreme overtime.	Medium	Medium	Extra time can be spent on the project during reading week to help get back on schedule. Development can be done iteratively, so there will be a working product at the end of the schedule. Stretch goals can be left to the end to make sure core functionality is complete	
3	Underestimating testing time	The debugging and integration testing of the project takes longer than anticipated.	Medium	Medium	Allocate more time to testing and start testing in parallel with development.	
4	Performance bottlenecks	The search or RSVP actions may exceed the 2 second performance requirement.	Low	Medium	Optimize queries and caching and test the performance under simulated loads early on in the project.	
1	Extreme winter conditions preventing team coordination	Canadians winters way impede vesicles used to get to team and sponsor meeting.	Medium	Low	Have winter tires and be prepared for Canadian winters and the risks thereof. Failing	

					the risks thereof. Failing that, a method to meet online can be prepared to use if in person meetings become impossible, presently that will be the project Discord.	

Deadline Report						
ID	Description	Submitter	Revised Finish Date	Reason for Change	Impact Analysis	Approved By
1	Incorporate the front end of the project.	Ashton	11/06/2025	Executive sponsor wants to see a 3-5 minute video of the front end.	The impact will be moderate we just have to switch from doing the backend first to front.	patricia.lasserre@ubc.ca

Decisions Report					
ID	Date of Decision	Description	Decision Made	Decision Maker(s)	Reason for Decision
1	10/26/25	Two-week Sprint	Incorporating the front end first	Ashton Raber, Dan Williams, Gabriel Traas	Executive sponsor wants to see a working prototype of the front end UI.

Issues Report						
ID	Issue Name	Description	Status	Impact	Mitigation/ Response Plan	Date Identified
1	Insufficient Developer Training	There are some programs and techstack items that no present developer within the project has used before, or which we are actively learning in other classes, this could potentially lead to slower production times as we learn the systems before they can be implemented.	In Progress	Medium	Each individual is responsible for their own training, with an understanding that we will reach out to each other in the event that the issue is begins to resulting in the slowing of production times. In this event additional manpower and expertise can be lent to that developer.	
2	Front End Sprint	The executive sponsor wants to see a compete UI prototype within 2 weeks with a 3-5 minute videos showcasing the front end.	In Progress	Medium	The team will switch the focus of working on the backend to incorporate the front end first.	

Deliverables Report					
ID	Name	Status	% Complete	Owner	Planned Finish Date
3.1.1.2	Create User, Event, Attendee, and Vendor tables	In Progress	60	Ashton Raber	10/30/25
3.1.1.4	Create simple homepage	In Progress	75	Gabriel Traas	10/29/25
3.1.1.5	Create simple event, vendor, account pages	In Progress	55	Ashton Raber, Dan Williams, Gabriel Traas	10/31/25

Scope Changes Report				
ID	Description	Reason for Change	Submission Date	Impact Analysis

