

P8 MILESTONE REVIEW

L03-Scrum&Coke:

Dan Williams

Ashton Raber

Gabriel Traas

MILESTONE DELIVERABLES

- **Technical Specification**
- **Database Schema Chosen**
- **Hosting Platform Chosen**
- **Project Wireframe**
- **Early Risk Identification**
- **Site Colours and Theme Selected**
- **Site Fonts Selected**
- **Create User, Event, Attendee, and Vendor Tables**
- **Create Simple Event, Vendor, Account Pages**
- **Create Simple Homepage**

CONDITION DEFINITIONS

Pass

- The deliverable meets all stated requirements and quality standards outlined in the project plan.

Conditional Pass

- The deliverable meets most requirements, but there are minor issues or omissions that must be addressed for full acceptance.

Fail

- The deliverable does not meet key project requirements or is incomplete, showing major deficiencies that prevent it from being accepted.

COMPLETION REVIEW

Non-Code

- Short peer discussion in discord, lab, or meeting.
- Compare against original requirements to determine completion

Code


- Github PR code reviews. Must be approved by at least 1 other member.
- Must pass all pytest before being merged

Smartsheet

- Weekly review meeting where we cross-check evidence, before changing completion percentages and updating dashboard

DELIVERABLES STATUS TIMELINE


P5 Deliverables Status

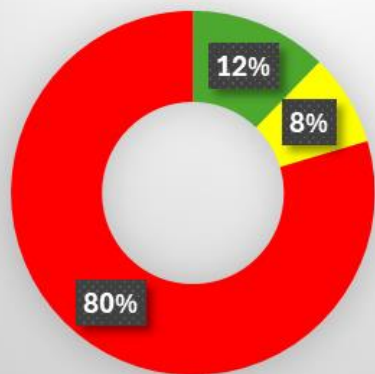

■ Complete
■ In Progress
■ Not Started




P6 Deliverables Status

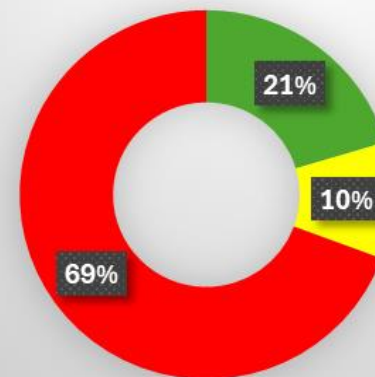

■ Complete
■ In Progress
■ Not Started

DELIVERABLES STATUS TIMELINE


P7 Deliverables Status

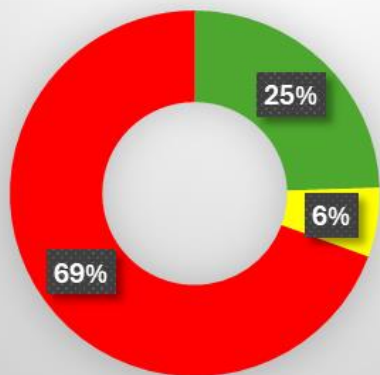

■ Complete
■ In Progress
■ Not Started




P8 Deliverables Status

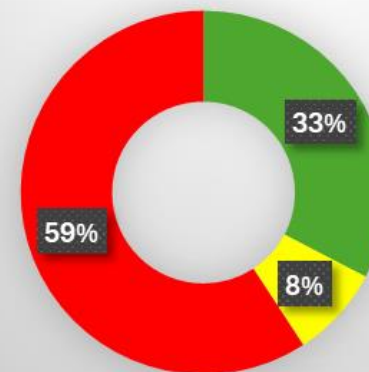

■ Complete
■ In Progress
■ Not Started

DELIVERABLES SUMMARY

Deliverables in Milestone

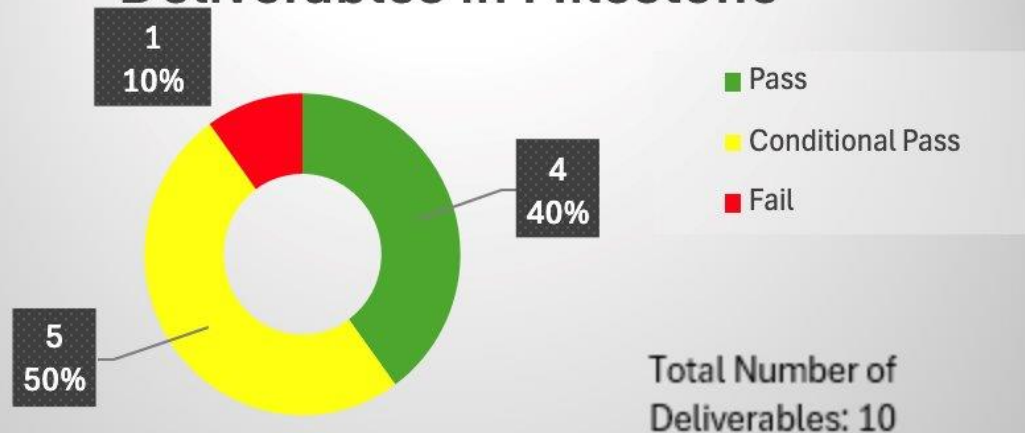


- Wireframe
- Main Colours Selected
- Create Simple Homepage
- Create Simple Event, Vendor, Account Pages

- Technical Specification
- Database Selected
- Early Risk Identification
- Fonts and Themes Selected
- Create User, Event, Attendee, and Vendor Tables

- Hosting Platform Selected


WEEK 5 SUMMARY

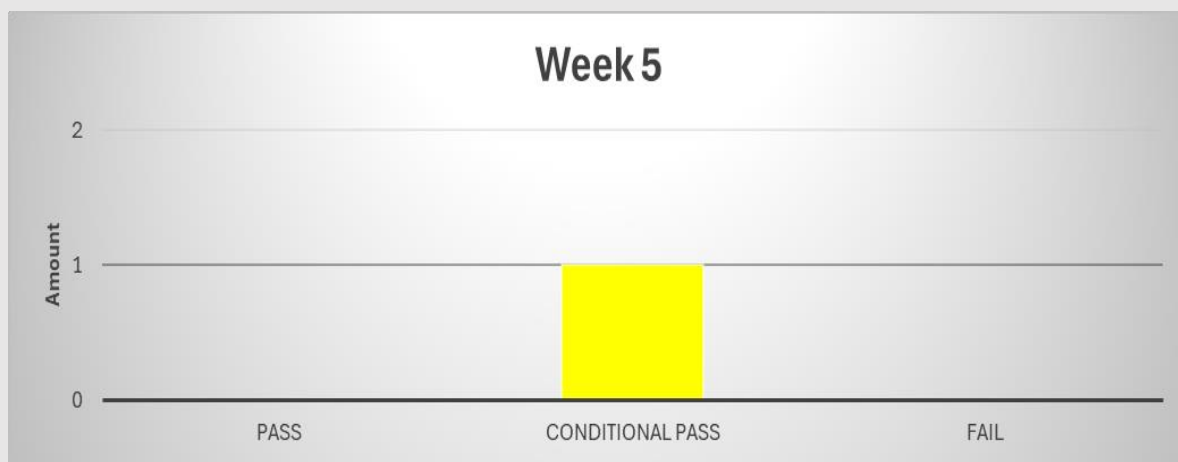

Technical Specification

Core tech stack and architecture are defined, but some implementation details and non-functional requirements are still being refined.

WEEK 6 SUMMARY

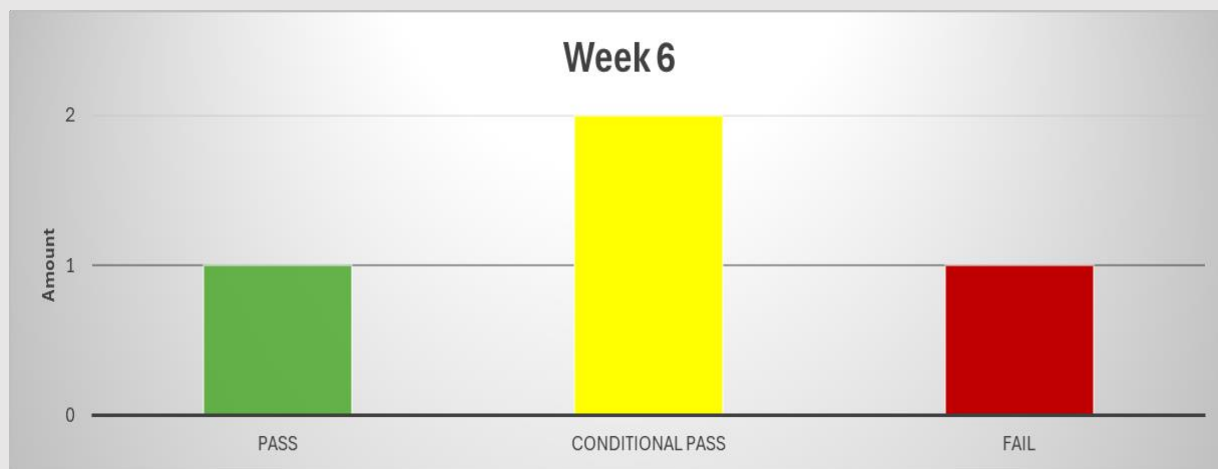

Wireframe

Core user flows are wireframed and align with agreed project scope.

Database Decided

SQLite chosen for now based on course experience, but not yet evaluated for scalability or deployment needs.


Early Risk Identification

Initial risk list created, but risks are not yet fully prioritized or assigned clear mitigation owners.

Hosting Platform Selected

Decision deferred while we addressed sponsor's video request and focused on frontend prototyping instead.

WEEK 7 SUMMARY

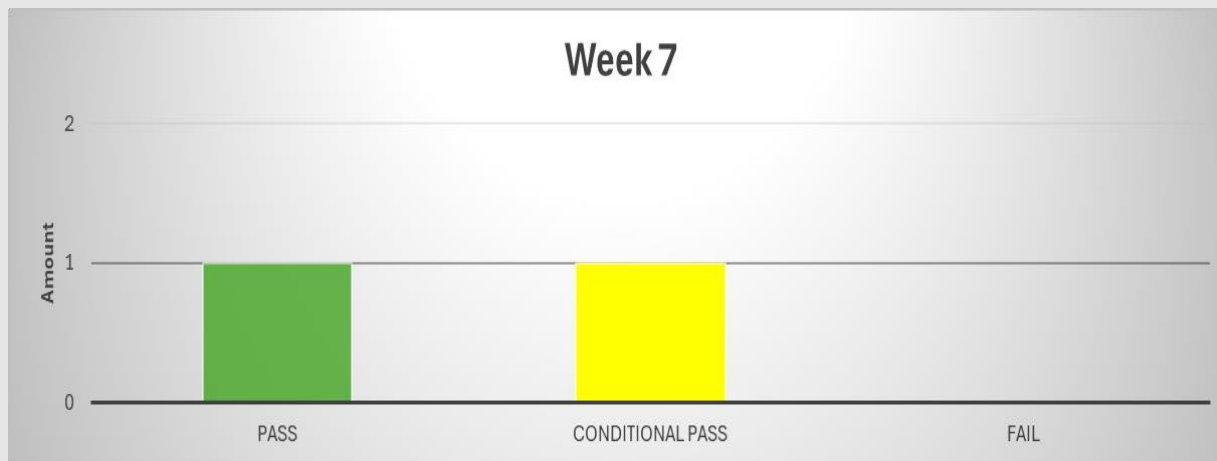


Site Colours Chosen

Primary colour palette and base layout style finalized and documented for use across the site.

Fonts and Themes Chosen

Initial font pairings and theme chosen, but readability/accessibility testing is still in progress.

WEEK 8 SUMMARY

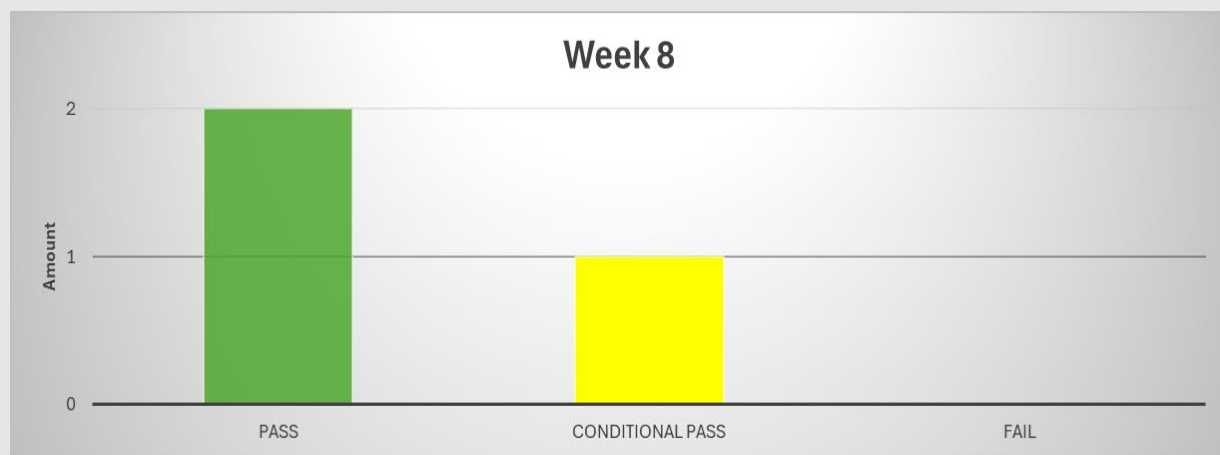

Create Simple Homepage

Basic homepage implemented with navigation and placeholder content for key sections.


Create Simple Event, Vendor, Account Pages

Simple event, vendor, and account pages built with core fields and linked into the main navigation.

Create User, Event, Attendee, and Vendor Tables

Created sample tables for presentation purposes. Actual tables for still need to be defined and created.

OVERALL DELIVERABLES MOVEMENT

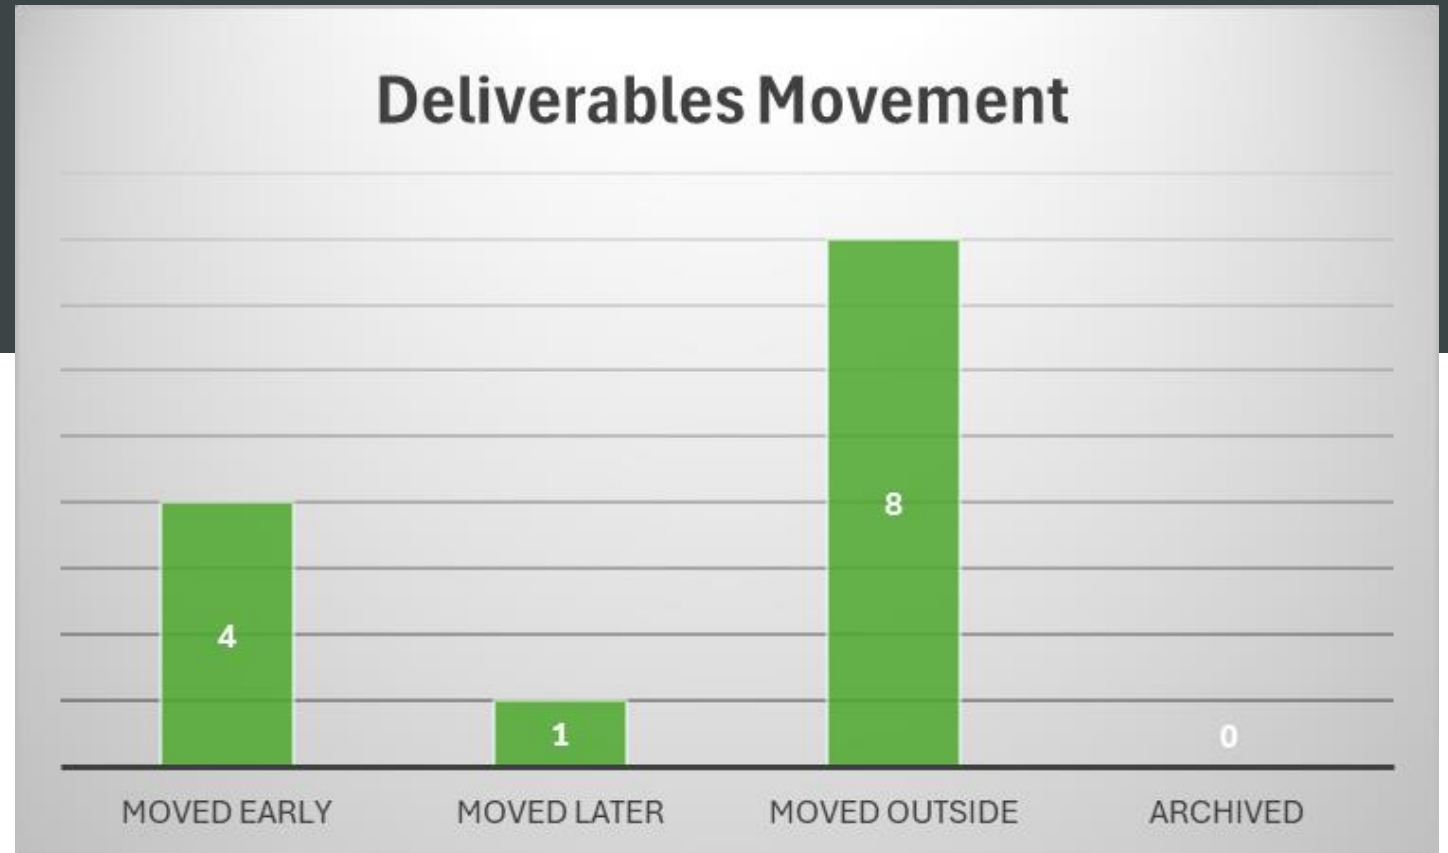

CHANGE REQUESTS


Deadline Change: Front End Prototype

- High impact since completing the front-end first may introduce dependencies and affect milestone alignment


Scope Change: All Optional Stretch Objectives must be Completed

- Minimal impact since the optional stretch objectives are now required, but they were already considered in the original scope and planning.

RISK STATUS DISTRIBUTION

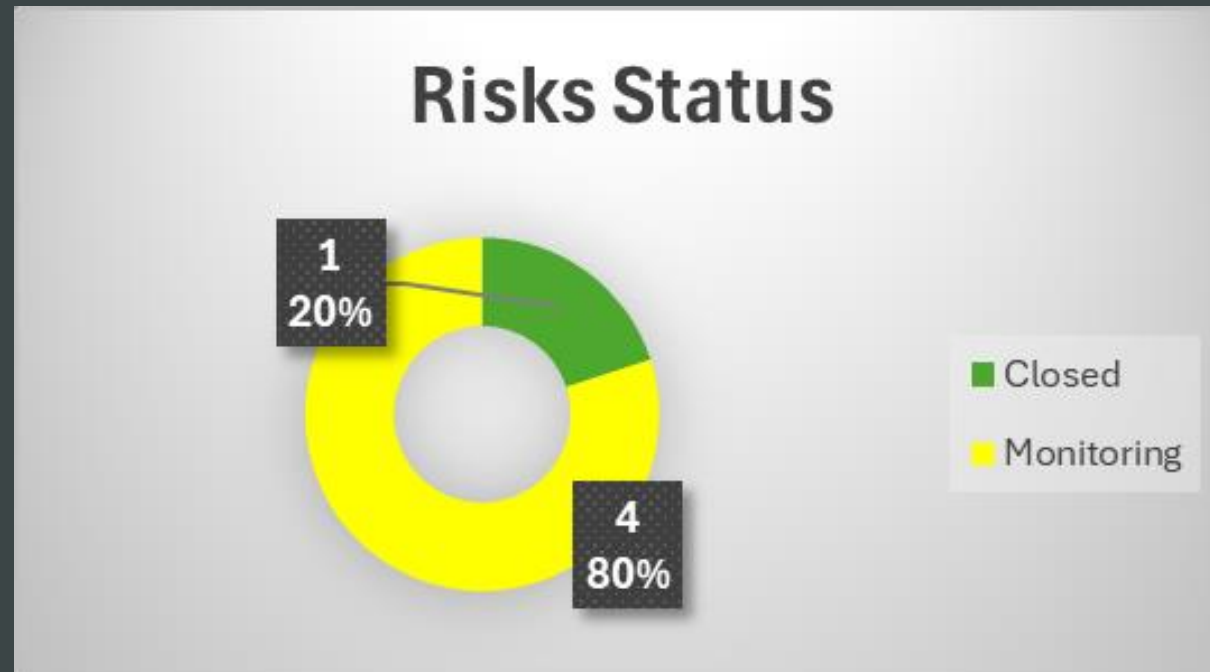

RISK
DISTRIBUTION
BY IMPACT AND
PROBABILITY

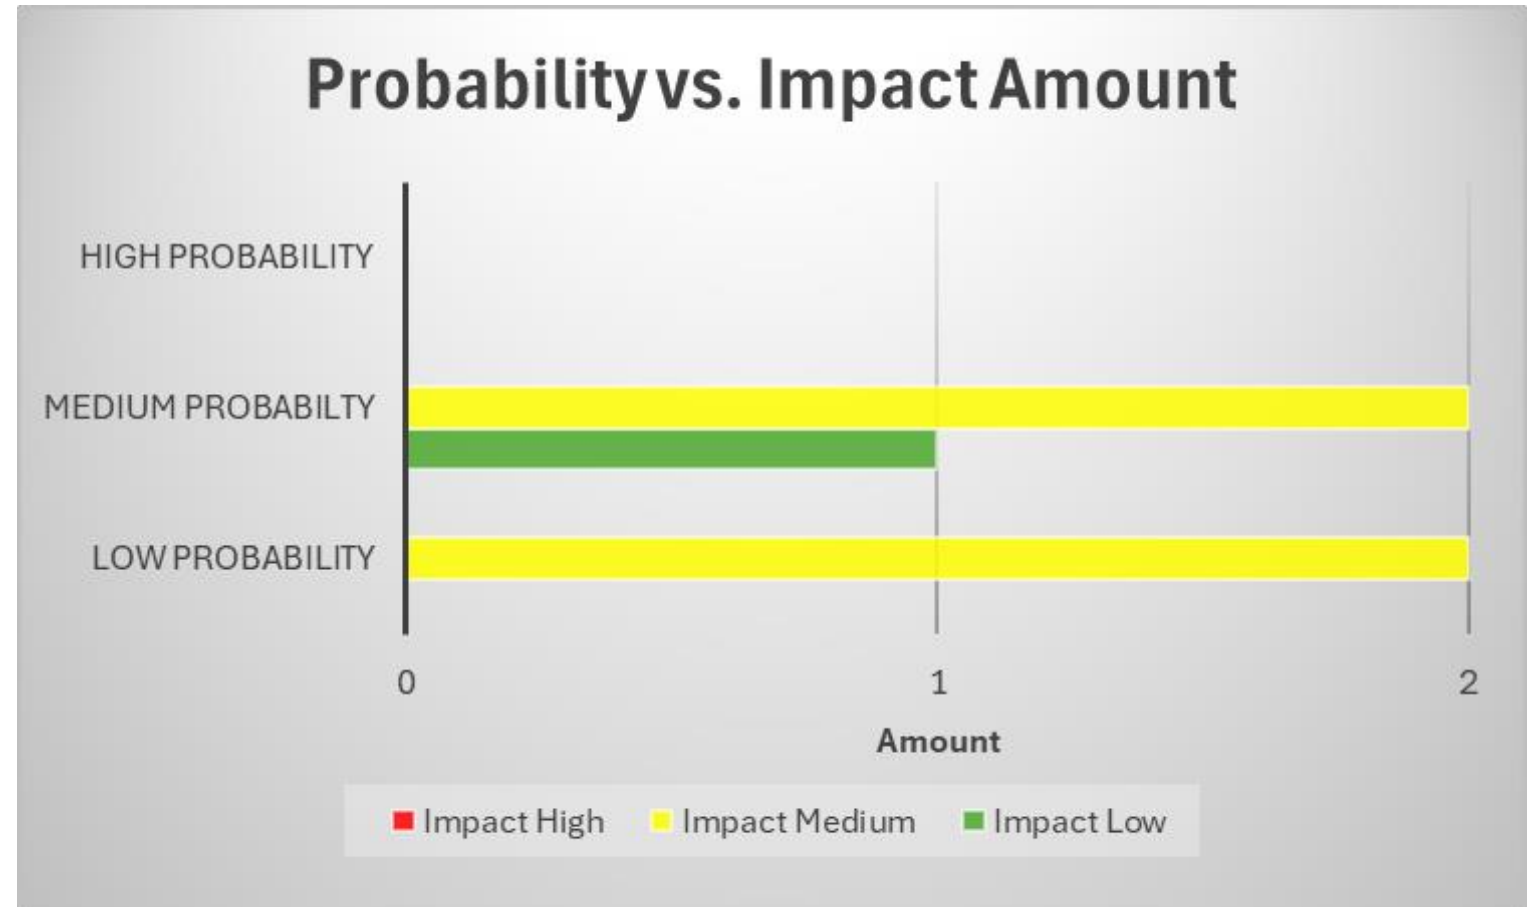

RISK SUMMARY TABLE

Legend

Low/ Closed



Medium/
Monitoring




High




Risk Name	Description	Impact	Probability	Status	Mitigation/ Response Plan	Notes
Extreme winter conditions preventing team coordination	Canadians winters way impede vesicles used to get to team and sponsor meeting.				Ensure team members are prepared for winter conditions (e.g., winter tires, travel safety). If in-person meetings become impractical, switch to virtual meetings using the project's Discord server.	The probability will be increasing as it start to snow.
Deadlines cannot be met	The deadlines of project deliverables are imminent and the development team agrees it is unlikely to be accomplished without extreme overtime.				Extra time can be spent on the project during reading week to help get back on schedule. Development can be done iteratively, so there will be a working product at the end of the schedule. Stretch goals can be left to the end to make sure core functionality is complete	
Underestimating testing time	The debugging and integration testing of the project takes longer than anticipated.				Allocate more time to testing and start testing in parallel with development.	
Performance bottlenecks	The search or RSVP actions may exceed the 2 second performance requirement.				Optimize queries and caching and test the performance under simulated loads early on in the project.	
Missing Stakeholder Feedback	Sponsor or instructor feedback was delayed, potentially leading to different interpretations of the project requirements.				The team will spend extra time going over each report and communicate with the TA to ensure the correct requirments are met.	


ISSUES STATUS DISTRIBUTION

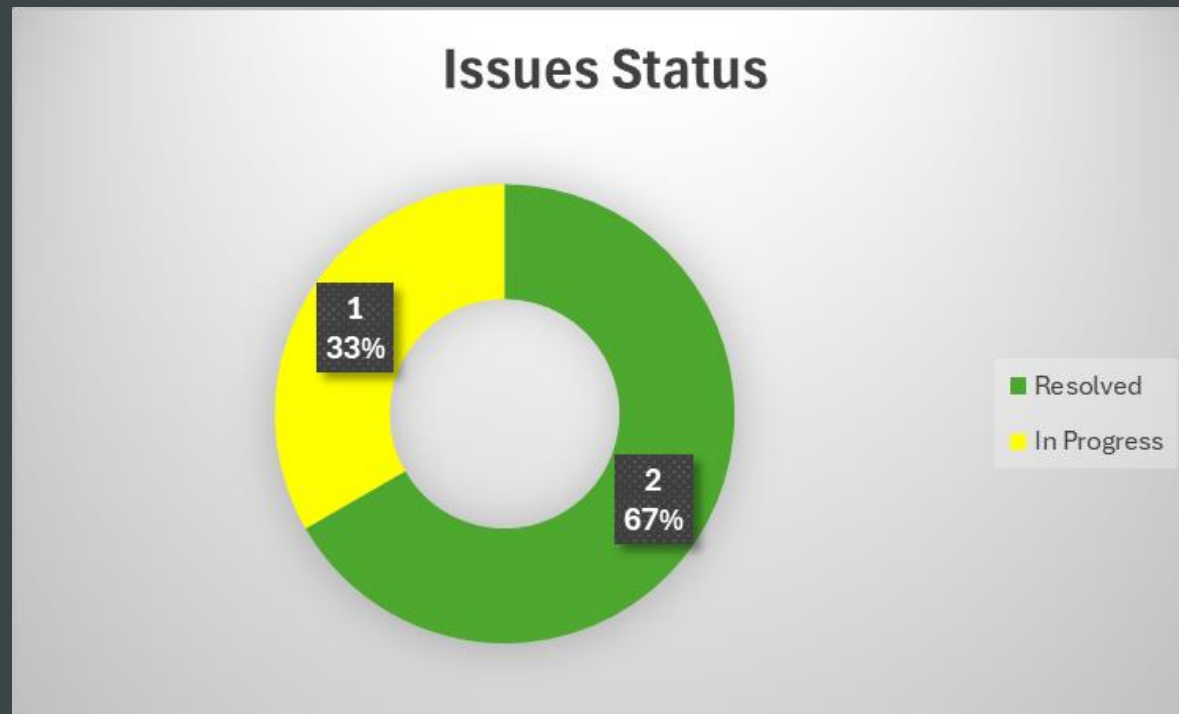

ISSUES
DISTRIBUTION
BY IMPACT

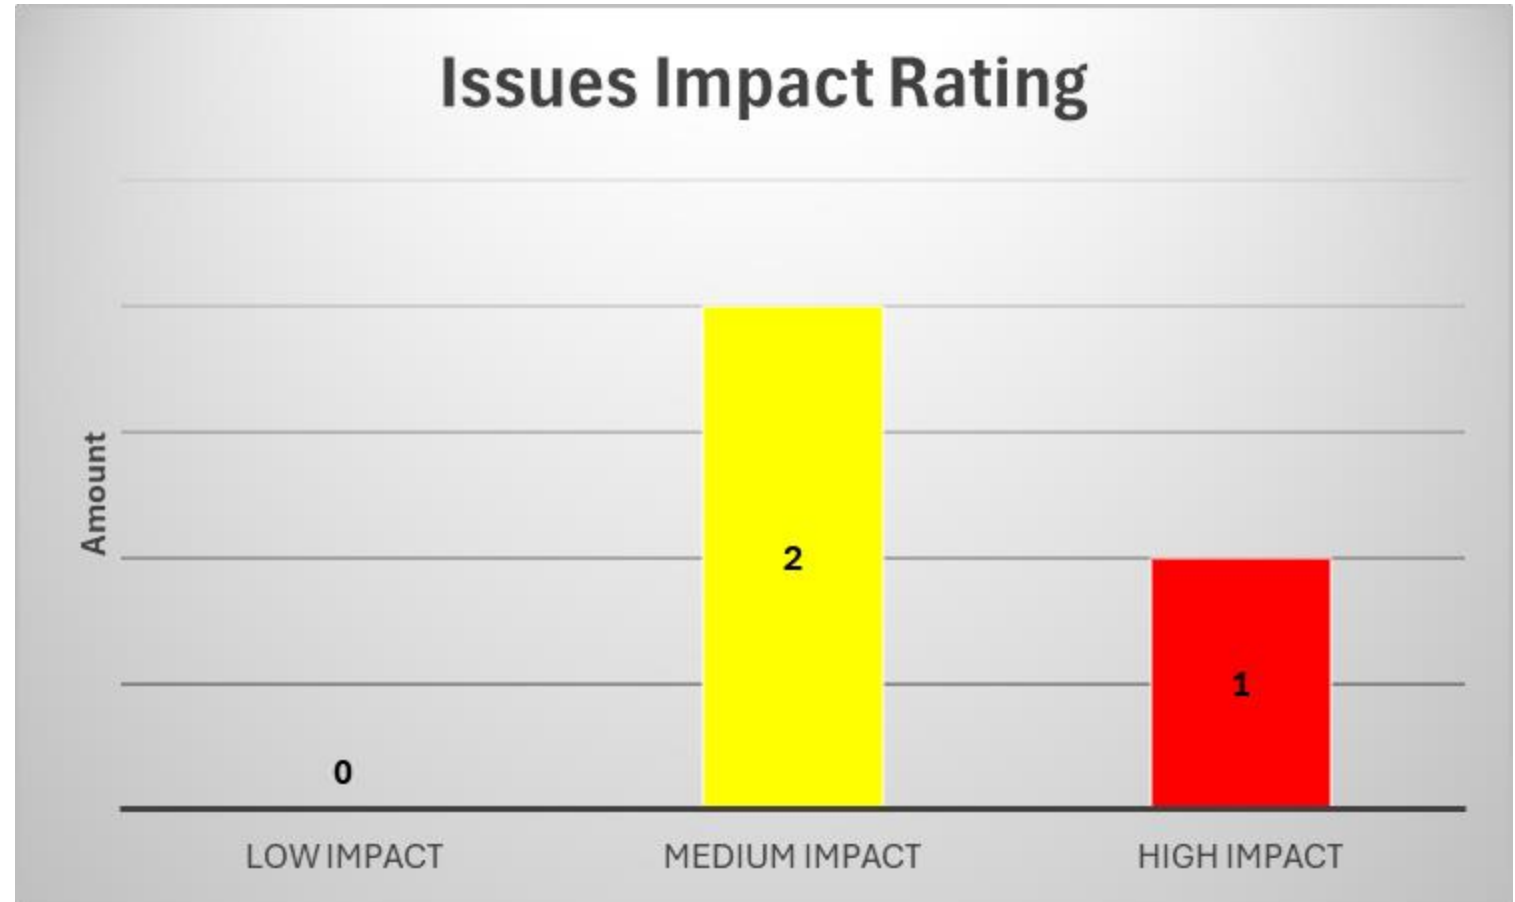

ISSUES
AVERAGE
IMPACT PER
CATEGORY

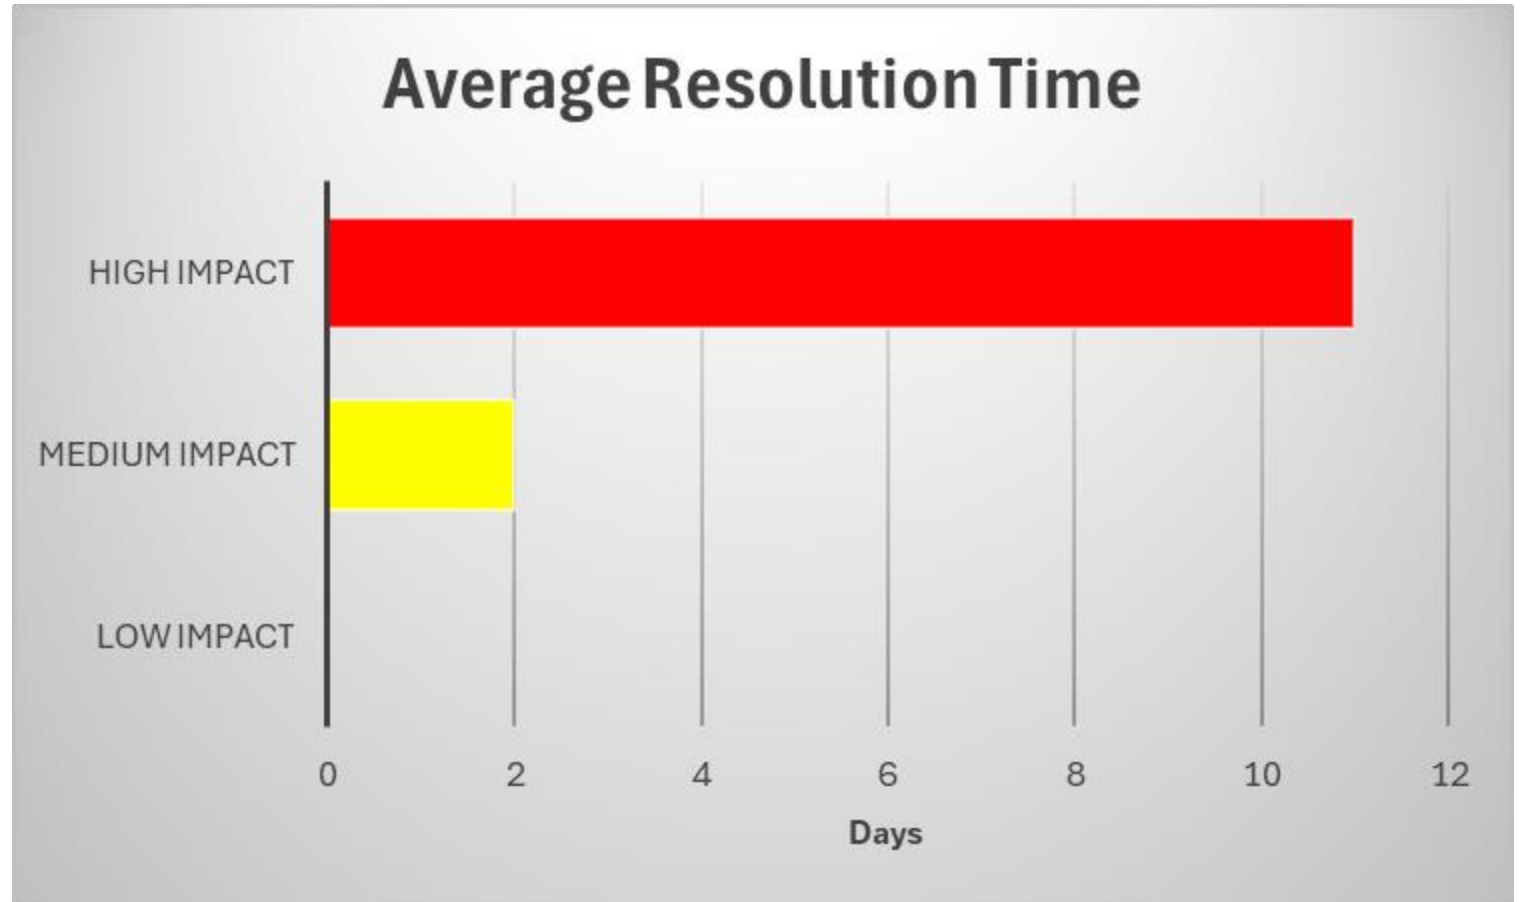

ISSUES SUMMARY TABLE

Legend	
Low/ Resolved	
Medium/ In Progress	
High	

Issues Name	Impact	Status	Resolution Duration (Days)
Insufficient Developer Training			
Front End Sprint			11
Midterm Exams			2

Status	Count	Average Time (Days)
Resolved	2	6.5

Improve Time and Workload

Planning

- Create more buffer time into the schedule and plan lighter workloads around known busy academic periods.

Manage Scope and Priorities More

Rigorously

- Confirm task order and dependencies early, and evaluate change request carefully to minimize disruption.

LESSONS
LEARNED
FROM
MILESTONE

THANK YOU

Scrum&Coke Development
