

P9 Dashboard


Weekly Summary

The project made significant progress this week compared to previous weeks. The team began developing the backend, implementing the database and several key features. Login functionality was connected through an API and integrated with the existing frontend. The system now supports login and logout capabilities, as well as the creation of new user accounts. Additionally, three of the required ten upcoming events were added to the database, all of which are now connected to the frontend through the API. The team also successfully completed the milestone review presentation, highlighting the progress made from P5 to P8.

Recent Deliverables Completed

ID	Name	Owner	Notes
3.1.1.1	Add API and database to project	Ashton Raber, Dan Williams	
3.1.1.3	Create backend login functionality	Dan Williams	
3.1.1.6	Connect login functionality via API	Ashton Raber, Dan Williams, Gabriel Traas	

Deliverables Status

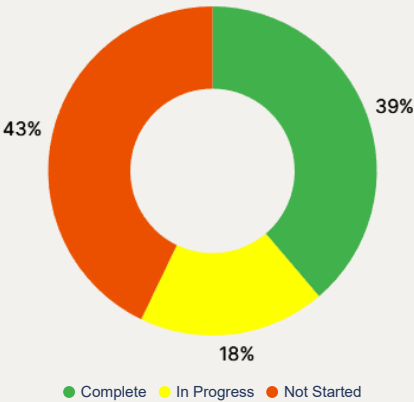

Gantt Chart Timeline

🔍 🔍 Months 📅



Risks Report

ID	Risk Name	Description	Impact	Probability	Mitigation/ Response Plan	Notes/ Updates
3	Underestimating testing time	The debugging and integration testing of the project takes longer than anticipated.	Medium	Medium	Allocate more time to testing and start testing in parallel with development.	
4	Performance bottlenecks	The search or RSVP actions may exceed the 2 second performance requirement.	Low	Medium	Optimize queries and caching and test the performance under simulated loads early on in the project.	
1	Extreme winter conditions preventing team coordination	Canadians winters way impede vesicles used to get to team and sponsor meeting.	Medium	Low	Have winter tires and be prepared for Canadian winters and the risks thereof. Failing that, a method to meet online can be prepared to use if in person meetings become impossible, presently that will be the project Discord.	
2	Deadlines cannot be	The deadlines of project deliverables are	Medium	High	Extra time can be spent	

	met	imminent and the development team agrees it is unlikely to be accomplished without extreme overtime.			on the project during reading week to help get back on schedule. Development can be done iteratively, so there will be a working product at the end of the schedule. Stretch goals can be left to the end to make sure core functionality is complete	
--	-----	--	--	--	---	--

Deadline Report						
ID	Description	Submitter	Revised Finish Date	Reason for Change	Impact Analysis	Approved By

Decisions Report					
ID	Date of Decision	Description	Decision Made	Decision Maker(s)	Reason for Decision

Issues Report						
ID	Issue Name	Description	Status	Impact	Mitigation/ Response Plan	Date Identified
1	Insufficient Developer Training	There are some programs and techstack items that no present developer within the project has used before, or which we are actively learning in other classes, this could potentially lead to slower production times as we learn the systems before they can be implemented.	In Progress	Medium	Each individual is responsible for their own training, with an understanding that we will reach out to each other in the event that the issue is begins to resulting in the slowing of production times. In this event additional manpower and expertise can be lent to that developer.	

Deliverables Report					
ID	Name	Status	% Complete	Owner	Planned Finish Date
3.1.2.1	Add functions for logout and delete account	In Progress	70	Gabriel Traas	11/05/25
3.1.2.2	Add function to edit account details	In Progress	0	Ashton Raber	11/04/25
3.1.2.3	Add functionality to frontend for user functions	In Progress	20	Ashton Raber, Dan Williams	11/06/25
3.1.3.1	Find 10 upcoming events to add to database	In Progress	30	Ashton Raber, Gabriel Traas	10/28/25
3.1.3.2	Add functions to create, edit and attend events to backend	In Progress	5	Dan Williams	11/03/25
3.1.3.3	Add found events to database	In Progress	50	Ashton Raber	11/05/25
3.1.3.4	Add search event function to backend	In Progress	0	Dan Williams, Gabriel Traas	11/17/25
3.1.3.5	Add event creation and deletion for admins and event hosts	In Progress	10	Gabriel Traas	11/06/25
3.1.3.6	Add functionality to frontend for event functions	In Progress	10	Ashton Raber, Gabriel Traas	11/06/25

Scope Changes Report				
ID	Description	Reason for Change	Submission Date	Impact Analysis

